
Learning Unit 9: The Project Manager, Project Teams and Organisational Structures

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

CHAPTER 10

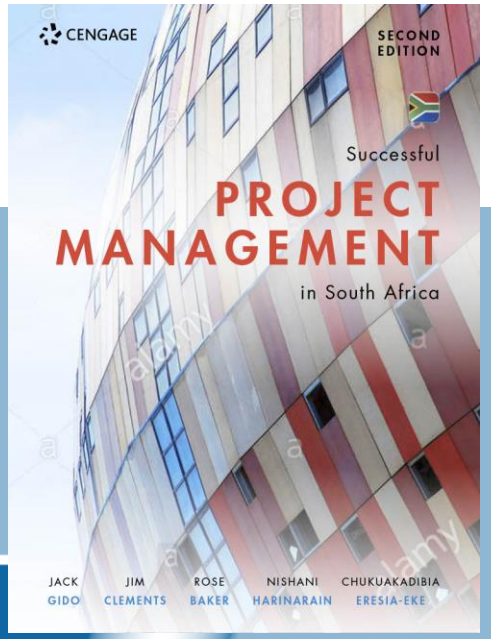

The Project Manager

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Chapter Concepts

- The responsibilities of the project manager
- The skills needed to successfully manage projects and ways to develop project manager competence
- Approaches to effective delegation
- How the project manager can manage and control changes to the project

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Learning Outcomes

- Discuss three responsibilities of a project manager
- Identify, explain, and practice at least five skills and abilities a project manager should have
- Explain how one would develop competence as a project manager
- Describe how one can effectively use delegation
- Explain how to manage changes

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Performance Domains of PMBOK® 7th edition covered in this chapter:		Knowledge Areas of PMBOK® 6th edition covered in this chapter:
• Stakeholders • Planning • Uncertainty • Team • Measurement	• Project Work • Development Approach and Life Cycle • Delivery	• Project Integration Management • Project Human Resource Management • Project Stakeholder Management

Project Management Principles relevant to this chapter

All 12 Principles

Principle 6 – Demonstrate Leadership Behaviours: Effective leadership, of both the individual and the team, is required in terms of vision, creativity and motivation to support project success and the team. Any team member can exhibit leadership behaviour. Leaders need to act with honesty and integrity, and ensure ethical conduct.

Principle 11 – Embrace Adaptability and Resiliency: The project team needs to be able to respond to change (adaptability) and to quickly recover from failures and setbacks (resilience) so that they can focus on outputs and ensure a successful project.

Principle 12 – Enable Change to Achieve the Envisioned Future State: Change is the transition of individuals, groups and organisations from the current state to a preferred future state. Project managers can keep an organisation prepared for change by acting as change agents and responding rapidly to changes that originate from both internal and external sources.

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Project Manager Responsibilities

- Customer satisfaction
- Work scope completion
  - Quality manner, within budget, on time
- Planning the project
- Securing and organising the appropriate resources
- Controlling the project progress
- Coordinate with team
- Control the project

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Planning

- Define project objective
- Reach agreement with customer
- Communicate objective to project team
- Create vision of successful achievement
- Spearhead plan development
- Review plan with customer
- Use project management information system

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Organising

- Secure appropriate resources
- Determine in-house tasks
- Determine need for subcontractor
- Assign responsibility
- Delegate authority
- Create motivating environment

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Controlling

- Track actual progress
- Compare progress to planned progress
- Take necessary actions
- Play the leadership role
- Involve project team

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Project Manager Skills: Leadership ability

- Achieve results through the project team
- Use a participative and consultative leadership style
- Provide guidance and coaching to the project team
- Require involvement and empowerment of the project team
- Establish an environment of trust, high expectations, and enjoyment
- Have self confidence
- Exhibit confidence in the project team

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Ability to develop people

- Train and develop the project team
- Believe that all individuals are valuable
- Encourage initiative
- Identify situations for mentoring
- Assess opportunities for growth
- Encourage self reflection for learning

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Communication skills

- Be good communicators
- Communicate and share information
- Spend more time listening than talking
- Inform the customer of progress
- Determine any changes
- Provide timely feedback to the team and customer

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Interpersonal skills

- Develop a relationship with each team member
- Maintain interpersonal relationships for duration of the project
- Influence the thinking and actions of others
- Deal with disagreements or divisiveness

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Ability to handle stress

- Must be able to handle the stress
- Remain calm
- Cope with constantly changing conditions
- Act as a buffer between the project team and either the customer or upper management
- Have a good sense of humour
- Keep physically fit to improve ability to handle stress

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Problem-solving skills

- Be a good problem solver
- Start with the early identification of a problem or potential problem
- Encourage project team members to identify problems early and solve them

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Negotiating skills

- Employ negotiating skills in interactions
- Develop a trusting relationship with the other person
- Use effective listening
- Take cultural differences into consideration
- Strengthen relationships, not erode them

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Time management skills

- Manage time well
- Have self-discipline
- Be able to prioritise
- Show a willingness to delegate

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Delegation

Delegating

- Empower the project team
- Use effective communication skills
- Select the most qualified project team members


Barriers to delegating

- Can do it better or faster yourself
- Lack confidence in the capability of others
- Afraid will lose control
- Fear criticism for mistakes
- Lack self-confidence

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Various degrees of delegation

FIGURE 10.1 Degrees of Delegation

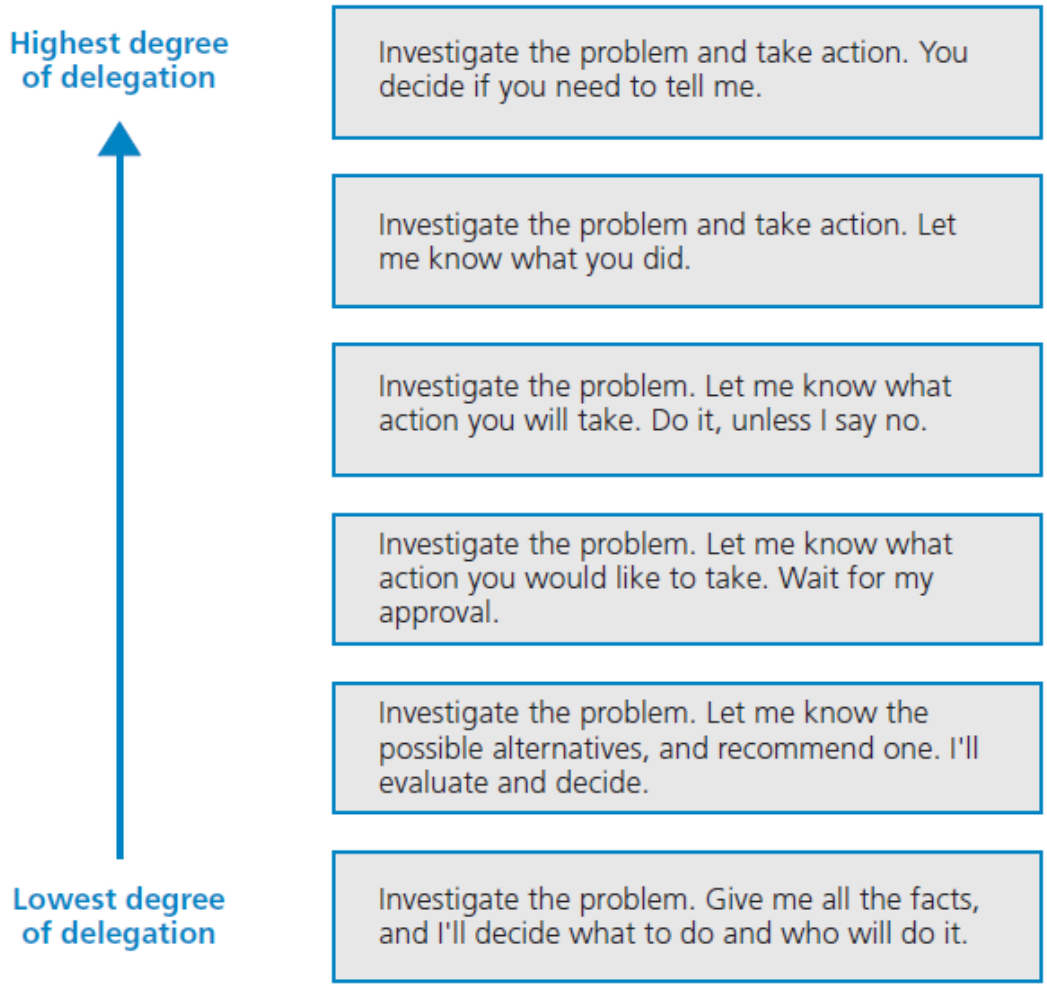

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Checklist for rating delegation effectiveness

FIGURE 10.2 Delegation Checklist

How effective are you at delegating?

	Not at all		Somewhat		Very much
1. Does your team have a clear understanding of the results expected?	1	2	3	4	5
2. Does your team have all the resources needed to accomplish what was delegated?	1	2	3	4	5
3. Do you focus on the results you expect from team members, rather than on the details of how they do their work?	1	2	3	4	5
4. Do you have a system to follow up and monitor progress?	1	2	3	4	5
5. Do team members understand how and when they are to let you know how they are progressing and when to seek your advice?	1	2	3	4	5
6. Does your team understand how progress will be measured and evaluated?	1	2	3	4	5
7. Can your team speak freely to you about problems, without fear of criticism?	1	2	3	4	5
8. Do team members feel they have the freedom to perform their work without you over-managing them?	1	2	3	4	5
9. Do team members feel they can perform their work without fear of making a mistake?	1	2	3	4	5
10. Do you encourage team members to make decisions within the level of authority you delegated to them?	1	2	3	4	5
11. Do you provide coaching as needed?	1	2	3	4	5
12. Do you encourage and are you supportive of your team's suggestions?	1	2	3	4	5

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Managing Changes

Initiation of change

- By the customer
- By the project team
- Caused by unanticipated occurrences
- Required by the users of the project results

Manage and control change

- Establish procedures for communication
- Estimate impact of change
- Decide about the change
- Customer approves change

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

CHAPTER 11

The Project Team

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Chapter Concepts

- How teams are acquired and assigned
- The development and growth of teams
- The project kick-off meeting
- Characteristics of effective project teams and barriers to effectiveness
- Being an effective team member
- Team building
- Valuing team diversity
- Ethical behaviour
- Sources of conflict during the project and approaches to handling conflict
- Problem solving and brainstorming
- Effective time management

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Learning Outcomes

- Explain how teams are assigned and formed
- Explain each stage of team development
- Plan and conduct a project kick-off meeting
- Discuss characteristics of effective teams
- Identify and describe at least five barriers to team effectiveness
- Be an effective team member
- Take actions to support team building
- Identify at least five dimensions of diversity, and discuss the value of team diversity
- Behave ethically in a project environment
- Identify at least four sources of conflict on projects, and explain how to handle conflict
- Apply the problem-solving process and the brainstorming technique
- Manage time effectively

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Performance Domains of PMBOK® 7th edition covered in this chapter:	Knowledge Areas of PMBOK® 6th edition covered in this chapter:
• Stakeholders • Team • Measurement	• Project Human Resource Management

Project Management Principles relevant to this chapter

Principle 1 (Be a Diligent, Respectful, and Caring Steward)
Principle 2 (Create a Collaborative Project Team Environment)
Principle 3 (Effectively Engage with Stakeholders)
Principle 7 (Tailor Based on Context)
Principle 9 (Navigate Complexity)
Principle 11 (Embrace Adaptability and Resiliency)
Principle 12 (Enable Change to Achieve the Envisioned Future State)

Principle 6 – Demonstrate Leadership Behaviours: Effective leadership, of both the individual and the team, is required in terms of vision, creativity and motivation to support project success and the team. Any team member can exhibit leadership behaviour. Leaders need to act with honesty and integrity and ensure ethical conduct.

Principle 11 – Embrace Adaptability and Resiliency: The project team needs to be able to respond to change (adaptability) and to quickly recover from failures and setbacks (resilience) so that they can focus on outputs and ensure a successful project.

Principle 12 – Enable Change to Achieve the Envisioned Future State: Change is the transition of individuals, groups and organisations from the current state to a preferred future state. Project managers can keep an organisation prepared for change by acting as change agents and responding rapidly to changes that originate from both internal and external sources.

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.


Acquiring the Project Team

- Project teams
  - What expertise, experience, or skills needed
  - How many of each type are required
  - When they will be needed
    - Acquire entire team for smaller projects
    - Assemble team members as needed for larger projects
- Greatest constraint is the availability of the right resources at the right time
- May have to negotiate for resources
- Keep team as small as feasible

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Project Team Development

FIGURE 11.1 Stages of Team Development

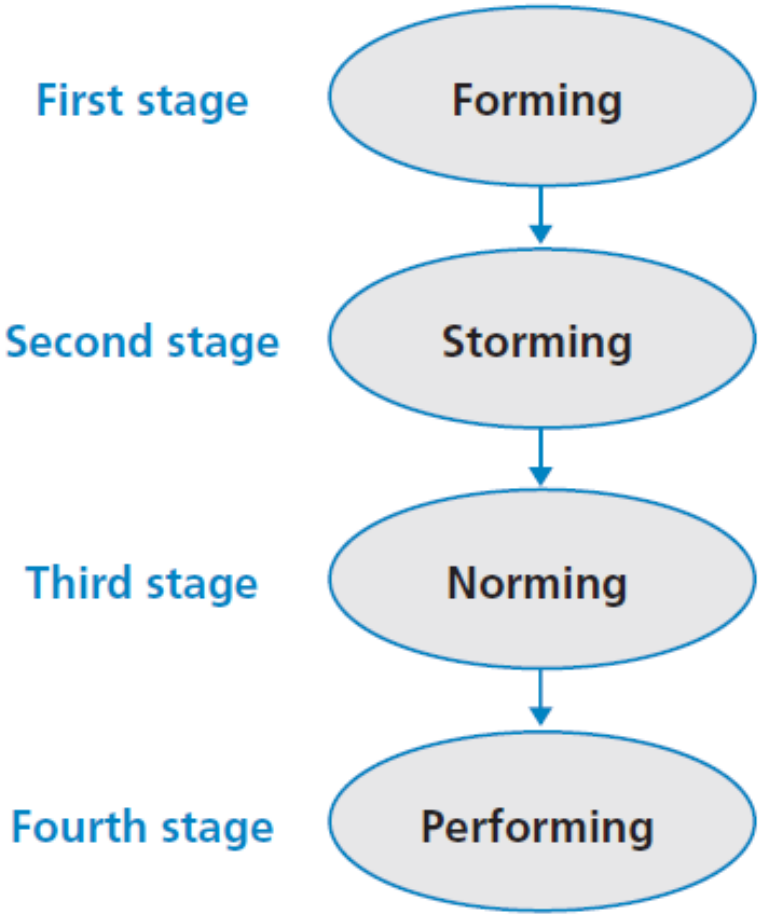


© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Forming

- Initial stage
- Individuals get acquainted
- Positive expectations
- Little work achieved
- Depend on direction and structure
- Lots of questions
  - What purpose?
  - Who are others?
  - What are they like?

FIGURE 11.2 Level of Functioning at Various Stages of Team Development

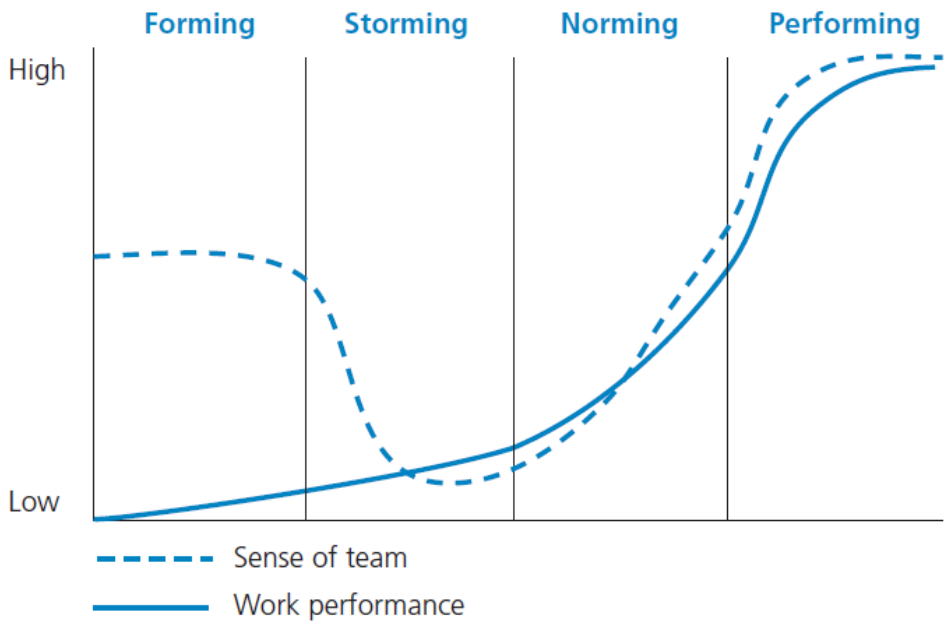


© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Storming

- Second stage
- Start to apply their skills to work
- Tasks may be larger than anticipated
- Increasing dissatisfaction with dependence
- Test the limits and flexibility of the team
  - Conflict emerges and tension increases
  - Motivation and morale are low
  - Members express individuality

FIGURE 11.2 Level of Functioning at Various Stages of Team Development

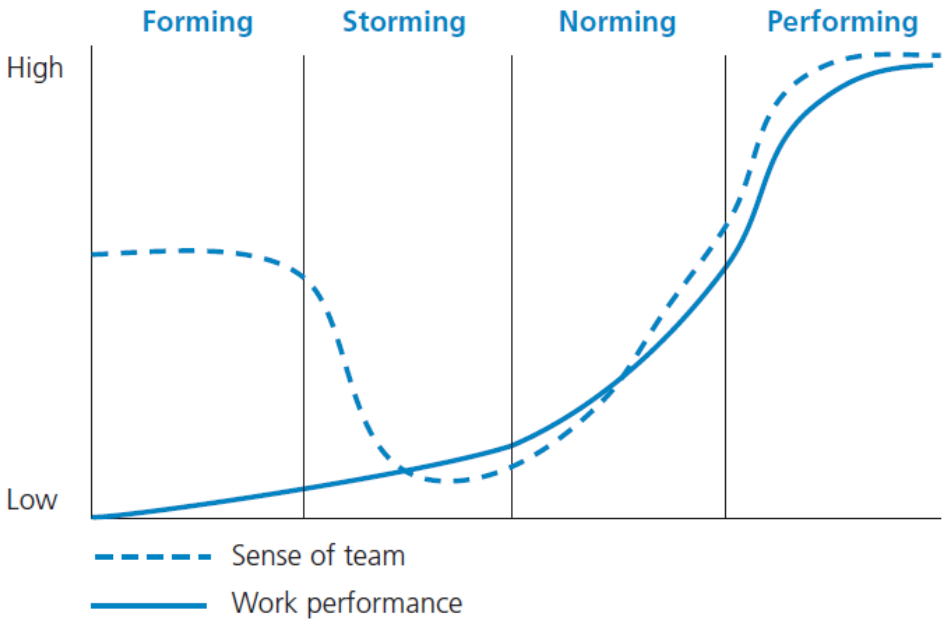


© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Norming

- Third stage
- Relationships have settled
- Interpersonal conflicts resolved
- Team has accepted its operating environment
- Control and decision making are transferred to the project team
- Cohesion begins to develop
- Trust begins to develop
- Team members give and ask for feedback
- Feeling of camaraderie emerges

FIGURE 11.2 Level of Functioning at Various Stages of Team Development

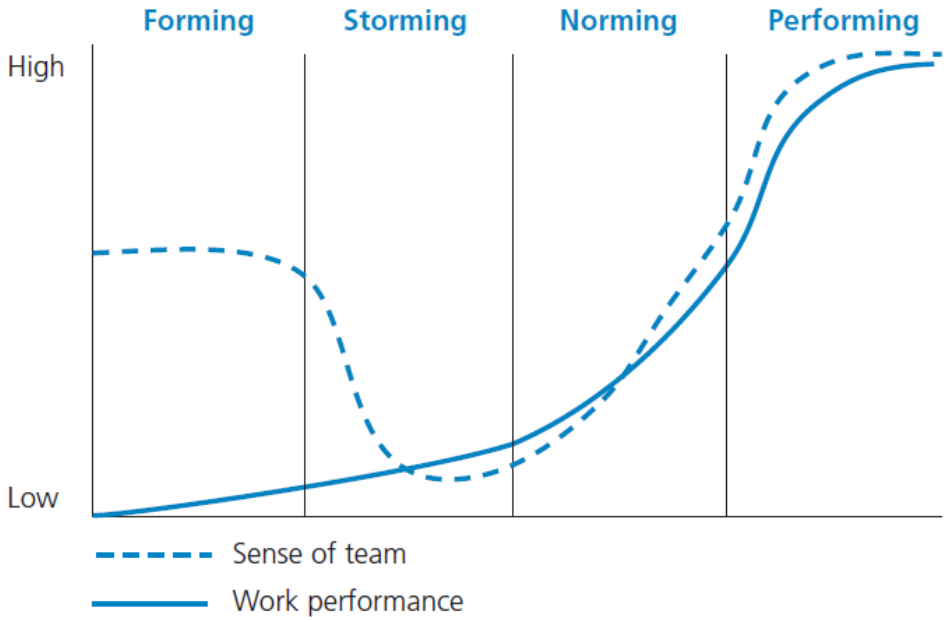


© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Performing

- Fourth stage
- High commitment to achieve project objective
- High level of work performance
- Communication is open
- Collaboration and willingness to help each other
- Team feels fully empowered
- Project manager fully delegates responsibility and authority
- Project manager is mentor

FIGURE 11.2 Level of Functioning at Various Stages of Team Development

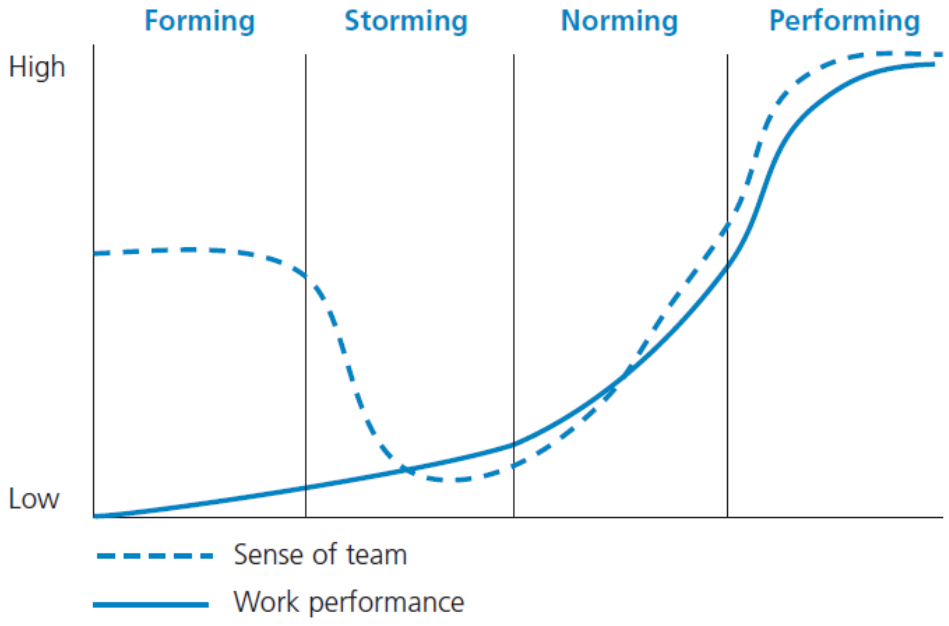

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Project Kick-off Meeting

- Project orientation
- Held as early as possible
- Sets the tone for the project
- Provides opportunity for team to know each other
- Clarify roles and responsibilities
- Describe protocols and plans
- Allow time for questions and comments

FIGURE 11.3 Project Kick-Off Meeting Agenda



© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Effective Project Teams

- More than a group of individuals
  - Group of interdependent individuals
  - Work cooperatively to achieve the project objective
- Develop and grow into a cohesive, effective team
  - Takes effort on the part of the project manager and each member

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Characteristics of effective teams

- Clear understanding of the project objective
- Clear expectations of each person's role and responsibilities
- Results orientation
- High degree of cooperation and collaboration
- High level of trust

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Rate team effectiveness

FIGURE 11.4 Team Effectiveness Checklist

How effective is your project team?

	Not at all			Somewhat	Very much
1. Does your team have a clear understanding of its goal?	1	2	3	4	5
2. Are the project scope, level of quality, budget and schedule well defined?	1	2	3	4	5
3. Does everyone have clear expectations of his or her own role and responsibilities?	1	2	3	4	5
4. Does everyone have clear expectations of other members' roles and responsibilities?	1	2	3	4	5
5. Does everyone know the expertise and skills that each person brings to the team?	1	2	3	4	5
6. Is your team results oriented?	1	2	3	4	5
7. Does everyone have a strong commitment to achieving the project objective?	1	2	3	4	5
8. Does your team have a high level of enthusiasm and energy?	1	2	3	4	5
9. Does your team have a high degree of cooperation and collaboration?	1	2	3	4	5
10. Are open, frank and timely communications the norm?	1	2	3	4	5
11. Do members readily share information, ideas and feelings?	1	2	3	4	5
12. Do members feel free to ask other members for help?	1	2	3	4	5
13. Do members willingly help one another?	1	2	3	4	5
14. Do team members give feedback and constructive criticism?	1	2	3	4	5
15. Do team members accept feedback and constructive criticism?	1	2	3	4	5
16. Is there a high level of trust among the project team members?	1	2	3	4	5
17. Do members follow through on what they say they will do?	1	2	3	4	5
18. Is there an openness to differing viewpoints?	1	2	3	4	5
19. Do team members accept one another and their differences?	1	2	3	4	5
20. Does your team constructively resolve conflicts?	1	2	3	4	5

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Team building

- An ongoing process
- The responsibility of both the project manager and the project team
- Socialising supports team building
- Enhanced by members getting to know one another
  - Discussions not all work related
  - Initiate social events to celebrate achievements
- Have team meetings, not just project meetings

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Valuing team diversity

- Acknowledge, understand, and value differences
  - Create a work environment that recognises, respects, and harnesses differences
  - Achieve a shared goal
- Differences can create barriers to team performance
  - May lead to miscommunication and misunderstanding
  - Can result in low morale, diminished trust, reduced productivity, greater tension, and suspicion
  - Can become a serious impediment, if not managed properly
- Under good management, diversity can lead to more creative, faster results, and higher-quality problem solving and decision making

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Valuing team diversity actions

Should NOT do

- Stereotype or make assumptions
- Exclude or have lower expectations
- Draw attention to diversity
- Make derogatory or insensitive remarks because it demeans the dignity of others
- Tell jokes, ridicule, or make fun

Should do

- Create and sustain a supportive and positive climate
- Develop a written diversity policy
- Provide diversity training
- Raise awareness and create understanding
- Help diminish misunderstanding and conflict
- Make a personal commitment to understand, value, and respect diversity

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Ethical Behaviour

- Opportunities for unethical behaviour
  - Some circumstances are debatable regarding misbehaviour
  - Project manager's responsibility to set the tone and expectations
- Actions to prevent wrongdoing
  - Have a policy on ethical behaviour
  - Conduct training sessions on ethical behaviour
- Non-threatening process to report any actions
- Members must feel accountable

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Key principles to guide ethical behaviour

- Treat others the way you want to be treated
- Don’t do anything you wouldn’t want your family, friends, neighbours, or co-workers to read about in the newspaper or hear on the news

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Conflicts on Projects

Sources of conflict

- Work scope
- Resource assignments
- Schedule
- Cost
- Priorities
- Organisational issues
- Stakeholder issues
- Personal differences

Handling conflict approaches

- Avoiding or withdrawing
- Competing or forcing
- Accommodating or smoothing
- Compromising
- Collaborating, confronting, or problem solving

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Problem Solving

- Nine-step approach
  1. Develop a problem statement
  2. Identify potential causes of the problem
  3. Gather data and verify the most likely causes
  4. Identify possible solutions
  5. Evaluate the alternative solutions
  6. Determine the best solution
  7. Revise the project plan
  8. Implement the solution
  9. Determine whether the problem has been solved

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Brainstorming

- All members of a group contribute spontaneous ideas in a non-judgmental environment
- Explore as broad a range of options and ideas
- The process
  - The team sits around a table, with a facilitator who records ideas
  - Member states an idea – do not discuss, justify, or try to sell it
  - Build on ideas previously mentioned
  - Continue until no one can come up with any more ideas or the time limit is up
- Two important rules must be followed
  - No immediate discussion of ideas
  - No judgmental comments
- Other participants are not allowed to make any comments at all, supportive or judgmental

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Time Management

- Identify goals to achieve the following week
- At the end of each day, make a to-do list for the next day
- Read to-do list first thing in the morning, and keep it in sight all day
- Control interruptions from the items on your to-do list
- Learn to say no to activities that will consume time but not contribute to achieving goals
- Make effective use of waiting time
- Try to handle most paperwork only once
- Go through incoming email or mail at the end of the day so that it will not divert from working on day's to-do list
- Take action on each mail document while holding it
- Reward at end of week if achieved all week's goals

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

CHAPTER 13

Project Management Organisational Structures

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Chapter Concepts

- The characteristics of the three types of organisational structures
- The advantages and disadvantages of each
- The role of a project management office

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Learning Outcomes

- Explain the three types of project management organisational structures
- Discuss the advantages and disadvantages of each type of project management organisational structure
- Describe the role of a project management office in a matrix organisational structure

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Performance Domains of PMBOK® 7th edition covered in this chapter:	Knowledge Areas of PMBOK® 6th edition covered in this chapter:
• Team • Planning • Uncertainty	• Project Integration Management • Project Human Resource Management

Project Management Principles relevant to this chapter

Principle 1 (Be a Diligent, Respectful, and Caring Steward)
Principle 2 (Create a Collaborative Project Team Environment)
Principle 3 (Effectively Engage with Stakeholders)
Principle 7 (Tailor Based on Context)
Principle 11 (Embrace Adaptability and Resiliency)
Principle 12 (Enable Change to Achieve the Envisioned Future State)

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.


Functional Organisational Structure

- Typically used in businesses that primarily sell and produce standard products
- Work groups consist of individuals who perform the same function
- Team members may be assigned to the project either full time or part time
- The project manager does not have complete authority over the project team
- Project manager regularly updates the other functional managers in the company on the status of the project

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Industrial business example: functional organisational structure

FIGURE 13.1 Functional Organisational Structure

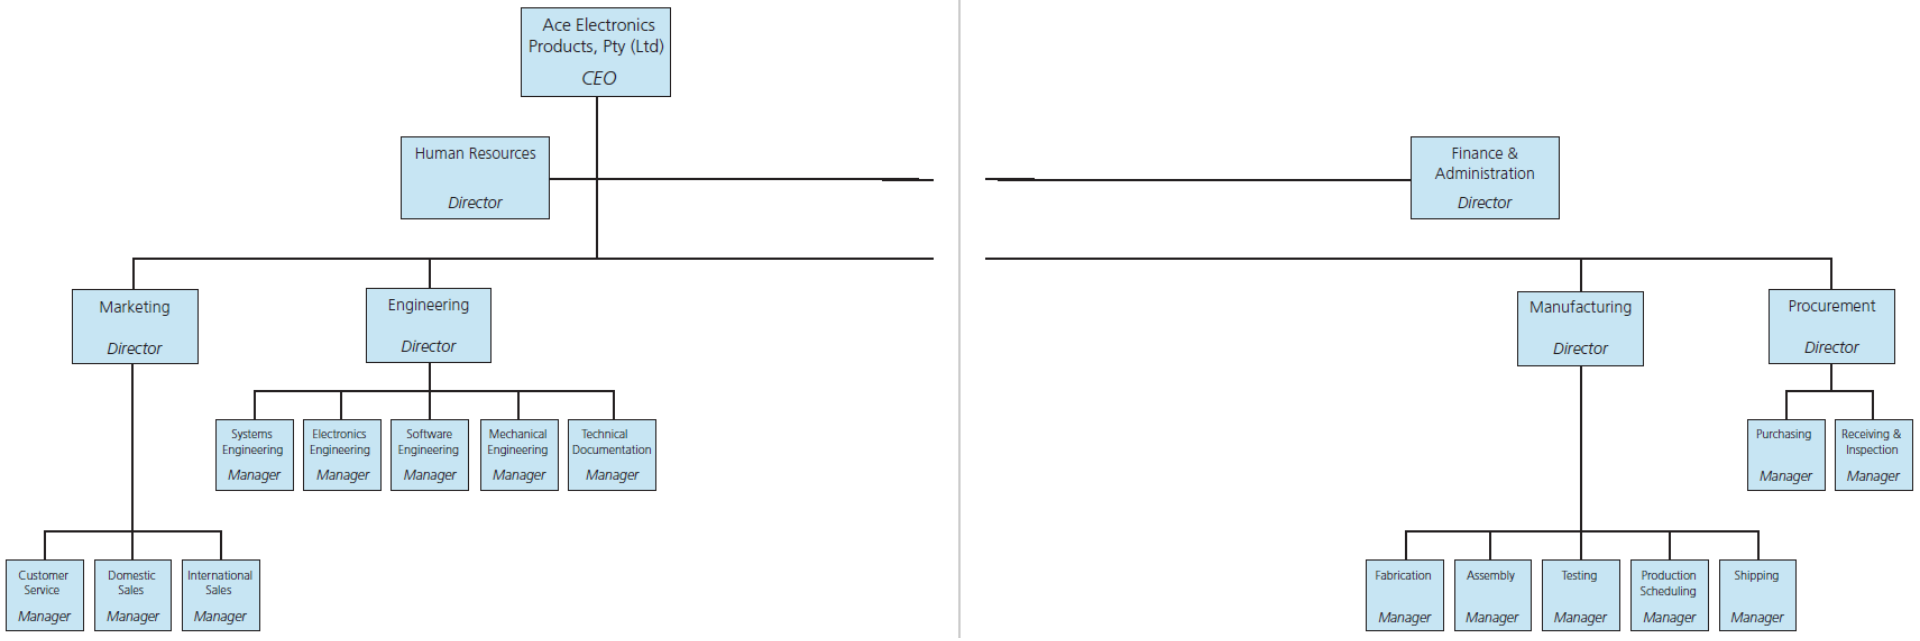

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.


Autonomous Project Organisational Structure

- Companies with this organisation are in the projects business; they do not produce standard products
- Company works on multiple projects at any given time; usually high Rand value and long term projects
- As projects are completed, the company hopes to get new contracts for projects
- Each project team is dedicated to only one project
- Each project is operated like a mini-company
- There is little opportunity for members of different project teams to share knowledge or technical expertise

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Rapid transit project business example: autonomous project organisational structure

FIGURE 13.2 Autonomous Project Organisational Structure

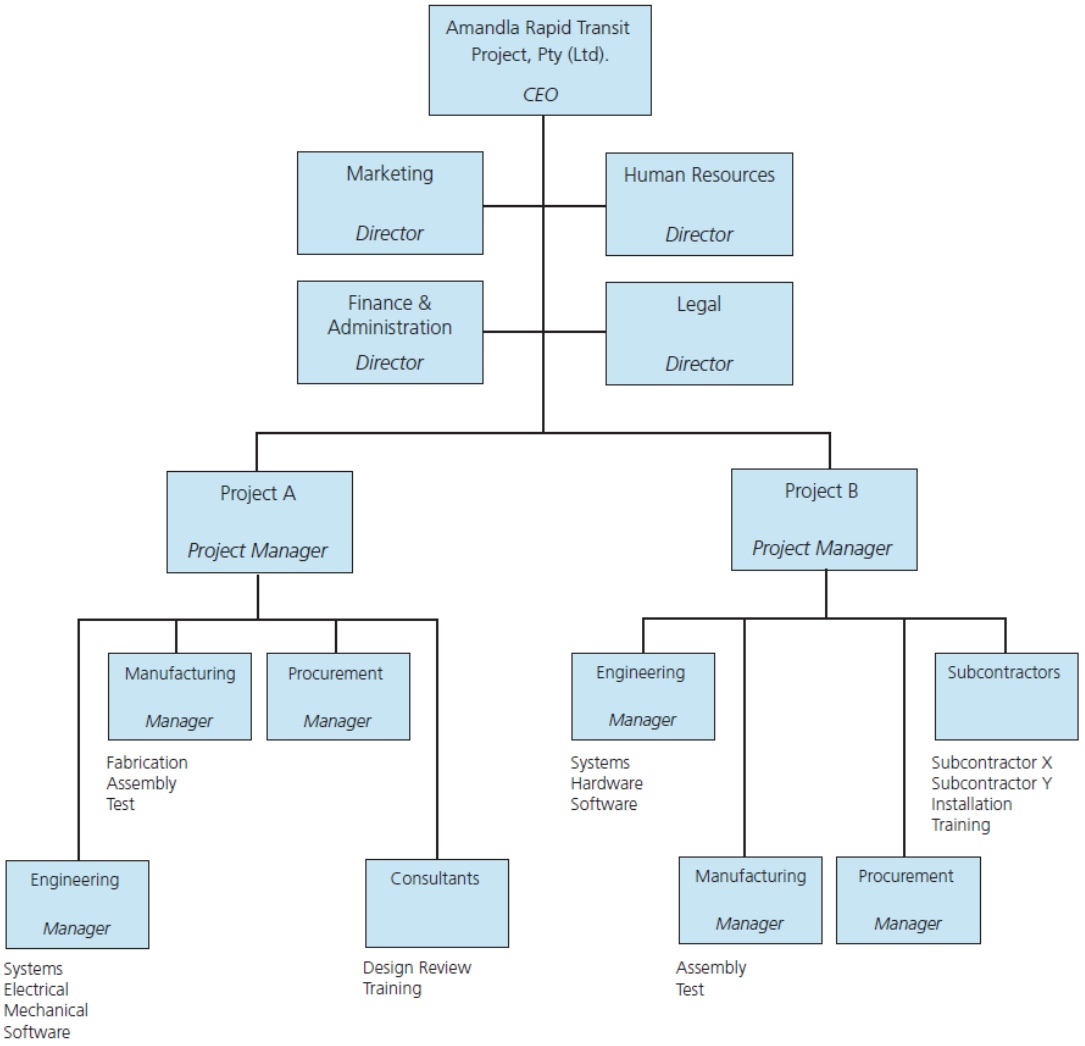

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.


Matrix Organisational Structure

- Multiple projects are in progress at any given time, and these projects vary in sise and complexity
- Hybrid structure—a mix of both the functional and autonomous project organisational structures
- Provides for effective utilisation of company resources
  - Employees assigned to the project for the length of time they are needed
  - Pursue career development through assignment to various types of projects
  - Have a dual reporting relationship—a (temporary) project manager and a (permanent) functional manager
- Project manager is the intermediary between the company and the customer
- Checks-and-balances and fast response upon problem identification

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Custom computer-based automation systems example: matrix organisational structure

FIGURE 13.3 Matrix Organisational Structure

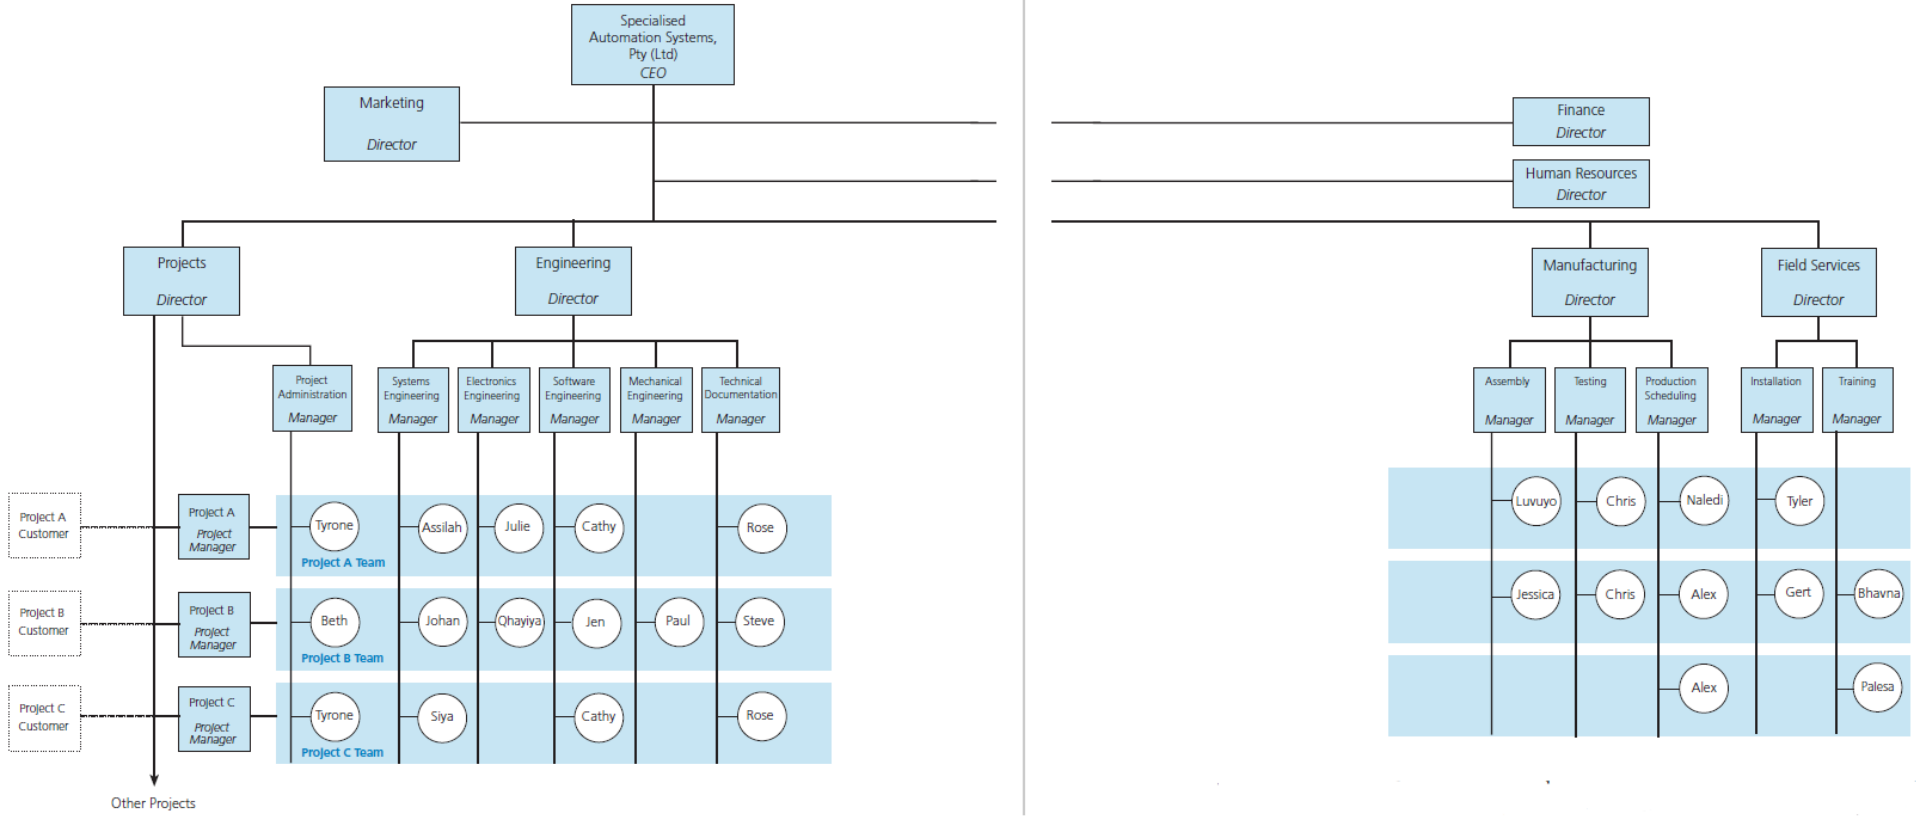

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Advantages and Disadvantages of Organisational Structures

TABLE 13.1 Advantages and Disadvantages of Organisational Structures

	Advantages	Disadvantages
Functional structure	• No duplication of activities • Functional excellence	• Insularity ('silo' tendency) • Slow response time • Lack of customer focus
Autonomous project structure	• Control over resources • Responsiveness to customers	• Cost inefficiency • Low level of knowledge transfer among projects
Matrix structure	• Efficient utilisation of resources • Functional expertise available to all projects • Increased learning and knowledge transfer • Improved communication • Customer focus	• Dual reporting relationships • Need for balance of power

© 2022 Cengage Learning. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.
